Rhyolite Ridge EIS Project Schedule

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	**Project Start Up**	**93 days**	**Mon 3/2/20**	**Fri 7/10/20**		
2	Notice of Award	0 days	Mon 3/2/20	Mon 3/2/20		BLM
3	MOU Signed	19 days	Mon 3/2/20	Thu 3/26/20	2	NEPA Team
4	Project Management Team Kick-off Meeting	0 days	Thu 4/9/20	Thu 4/9/20	2FS+10 days,3FS+	NEPA Team
5	Plan of Operations Submitted	0 days	Sun 5/10/20	Sun 5/10/20		Ioneer
6	BLM Review of Plan of Operations	30 edays	Sun 5/10/20	Tue 6/9/20	5	BLM,Stantec
7	Ioneer Revises Plan of Operations	10 days	Tue 6/9/20	Mon 6/22/20	6	Ioneer
8	Remaining Baseline Reports Submitted	0 days	Sun 5/10/20	Sun 5/10/20		Ioneer
9	BLM Review of Baseline Reports	30 edays	Sun 5/10/20	Tue 6/9/20	8	BLM,Stantec
10	Revisions to Baseline Reports	10 days	Tue 6/9/20	Mon 6/22/20	9	Ioneer
11	Plan and Baseline Deemed Complete	15 days	Fri 6/19/20	Fri 7/10/20	7,10	BLM
12	**Pre-Scoping**	**121 days**	**Fri 7/10/20**	**Tue 1/12/21**		
13	BLM and Cooperating Agency Pre-Scoping (Project Kick-off Meeting)	0 days	Fri 7/10/20	Fri 7/10/20	2,11	NEPA Team
14	Develop Preparation Plan	5 days	Mon 7/13/20	Fri 7/17/20	4,11	Stantec
15	BLM Review of Preparation Plan	5 days	Mon 7/20/20	Fri 7/24/20	14	BLM
16	Finalize Preparation Plan	3 days	Mon 7/27/20	Wed 7/29/20	15	Stantec
17	Preliminary Alternatives Development in Coordination with BLM and Ioneer	5 days	Mon 7/13/20	Fri 7/17/20	11,13	NEPA Team
18	Stantec Prepares Draft SERs	30 days	Thu 7/30/20	Thu 9/10/20	11,17,16	Stantec
19	BLM Reviews Draft SERs	15 days	Fri 9/11/20	Thu 10/1/20	18	BLM
20	Stantec Revises Draft SERs	10 days	Fri 10/2/20	Thu 10/15/20	19	Stantec
21	BLM Reviews/Accepts SERs	10 days	Fri 10/16/20	Thu 10/29/20	20	BLM
22	Stantec Prepares ADEIS	10 days	Fri 10/30/20	Fri 11/13/20	21	Stantec
23	BLM Reviews ADEIS	10 days	Mon 11/16/20	Tue 12/1/20	22	BLM
24	Stantec Revises ADEIS	3 days	Wed 12/2/20	Fri 12/4/20	23	Stantec
25	Stantec Prepares NOI Briefing Documents	2 days	Fri 10/30/20	Mon 11/2/20	21	Stantec
26	BLM Reviews NOI Briefing Documents	2 days	Tue 11/3/20	Wed 11/4/20	25	BLM
27	Stantec Revises NOI Briefing Documents	2 days	Thu 11/5/20	Fri 11/6/20	26	Stantec
28	BLM Nevada State Office and Regional Solicitor Review of ADEIS and NOI Briefing Documents	5 days	Mon 12/7/20	Fri 12/11/20	24,27	NEPA Team
29	Stantec Revises ADEIS from Solicitor Review	3 days	Mon 12/14/20	Wed 12/16/20	28	Stantec
30	BLM Approves ADEIS and Schedules Review Team Briefing	2 days	Thu 12/17/20	Fri 12/18/20	29	BLM,NEPA Team
31	Review Team Briefing NOI Clearance	10 days	Mon 12/21/20	Tue 1/12/21	30	NEPA Team
32	**NEPA Analysis**	**247 days**	**Tue 1/12/21**	**Thu 12/23/21**		
33	NOI Published in Federal Register	0 days	Tue 1/12/21	Tue 1/12/21	31	NEPA Team
34	Public Scoping Period	30 edays	Tue 1/12/21	Thu 2/11/21	33	NEPA Team
35	Prepare Scoping Materials	5 days	Wed 1/13/21	Tue 1/19/21	33	Stantec
36	BLM Review/Approve Scoping Materials	5 days	Wed 1/20/21	Tue 1/26/21	35	BLM
37	Public Scoping Meetings	4 days	Fri 3/5/21	Wed 3/10/21	34FS+15 days	NEPA Team
38	Prepare Scoping Summary Report	10 days	Thu 3/11/21	Wed 3/24/21	37	Stantec
39	BLM Reviews Scoping Summary Report	5 days	Thu 3/25/21	Wed 3/31/21	38	BLM
40	Stantec Revises Scoping Summary Report	5 days	Thu 4/1/21	Wed 4/7/21	39	Stantec
41	BLM Reviews/Approves Scoping Summary Report	2 days	Thu 4/8/21	Fri 4/9/21	40	BLM
42	Stantec Prepares PDEIS	15 days	Mon 4/12/21	Fri 4/30/21	34SF,41	Stantec
43	BLM Reviews PDEIS	5 days	Mon 5/3/21	Fri 5/7/21	42	BLM
44	Stantec Revises PDEIS	5 days	Mon 5/10/21	Fri 5/14/21	43	Stantec
45	Stantec Prepares NOA Briefing Package	5 days	Mon 5/10/21	Fri 5/14/21	43	Stantec
46	BLM Reviews NOA Briefing Package	5 days	Mon 5/17/21	Fri 5/21/21	45	BLM
47	Stantec Revises NOA Briefing Package	2 days	Mon 5/24/21	Tue 5/25/21	46	Stantec
48	BLM Nevada State Office and Regional Solicitor Review of PDEIS and NOA Briefing Package	5 days	Wed 5/26/21	Tue 6/1/21	47	NEPA Team
49	Stantec Revises PDEIS and Prepares Camera-Ready DEIS	3 days	Wed 6/2/21	Fri 6/4/21	48	Stantec
50	BLM Approves Camera Ready DEIS and Schedules Review Team Briefing	3 days	Mon 6/7/21	Wed 6/9/21	49	NEPA Team
51	Executive Review Team Briefing Camera Ready DEIS/NOA Clearance	10 days	Thu 6/10/21	Wed 6/23/21	50	NEPA Team
52	File DEIS with EPA eNEPA	1 day	Mon 7/5/21	Mon 7/5/21	51FS+7 days	BLM
53	NOA Published in the Federal Register	0 days	Tue 7/13/21	Tue 7/13/21	52FS+6 days	BLM
54	DEIS Public Comment Period	45 edays	Tue 7/13/21	Fri 8/27/21	53	NEPA Team
55	Public Comment Meetings	4 days	Wed 8/4/21	Mon 8/9/21	53FS+15 days	NEPA Team
56	Prepare Comment Analysis and Prepare AFEIS	20 days	Tue 8/10/21	Mon 9/6/21	55	Stantec
57	BLM Reviews Comment Responses and AFEIS	10 days	Tue 9/7/21	Mon 9/20/21	56	BLM
58	Stantec Drafts ROD	10 days	Tue 9/7/21	Mon 9/20/21	56	Stantec
59	Stantec Revises AFEIS and Prepares Camera Ready FEIS	5 days	Tue 9/21/21	Mon 9/27/21	57	Stantec
60	Stantec Prepares FEIS NOA Briefing Package	3 days	Tue 9/21/21	Thu 9/23/21	58	Stantec
61	BLM Reviews and Accepts Camera Ready FEIS, ROD and NOA Briefing Package	5 days	Tue 9/28/21	Mon 10/4/21	58,59,60	BLM
62	BLM Nevada State Office and Regional Solicitor Review of Camera-Ready AFEIS, ROD and NOA Briefing Package	5 days	Tue 9/28/21	Mon 10/4/21	59	NEPA Team
63	Stantec Revises and Prepares Camera-Ready FEIS	3 days	Tue 10/5/21	Thu 10/7/21	62	Stantec
64	BLM Approves Camera Ready FEIS and Schedules Review Team Briefing	5 days	Fri 10/8/21	Thu 10/14/21	63	NEPA Team
65	Executive Review Team Briefing Camera Ready FEIS/ROD/NOA Clearance	10 days	Wed 10/20/21	Tue 11/2/21	64FS+3 days	NEPA Team
66	File FEIS with EPA eNEPA	1 day	Mon 11/8/21	Mon 11/8/21	65FS+3 days	NEPA Team
67	NOA Published in the Federal Register	1 day	Tue 11/16/21	Tue 11/16/21	66FS+5 days	NEPA Team
68	FEIS Availability Period	30 edays	Tue 11/16/21	Thu 12/16/21	67	NEPA Team
69	Issue ROD	5 days	Fri 12/17/21	Thu 12/23/21	68	BLM

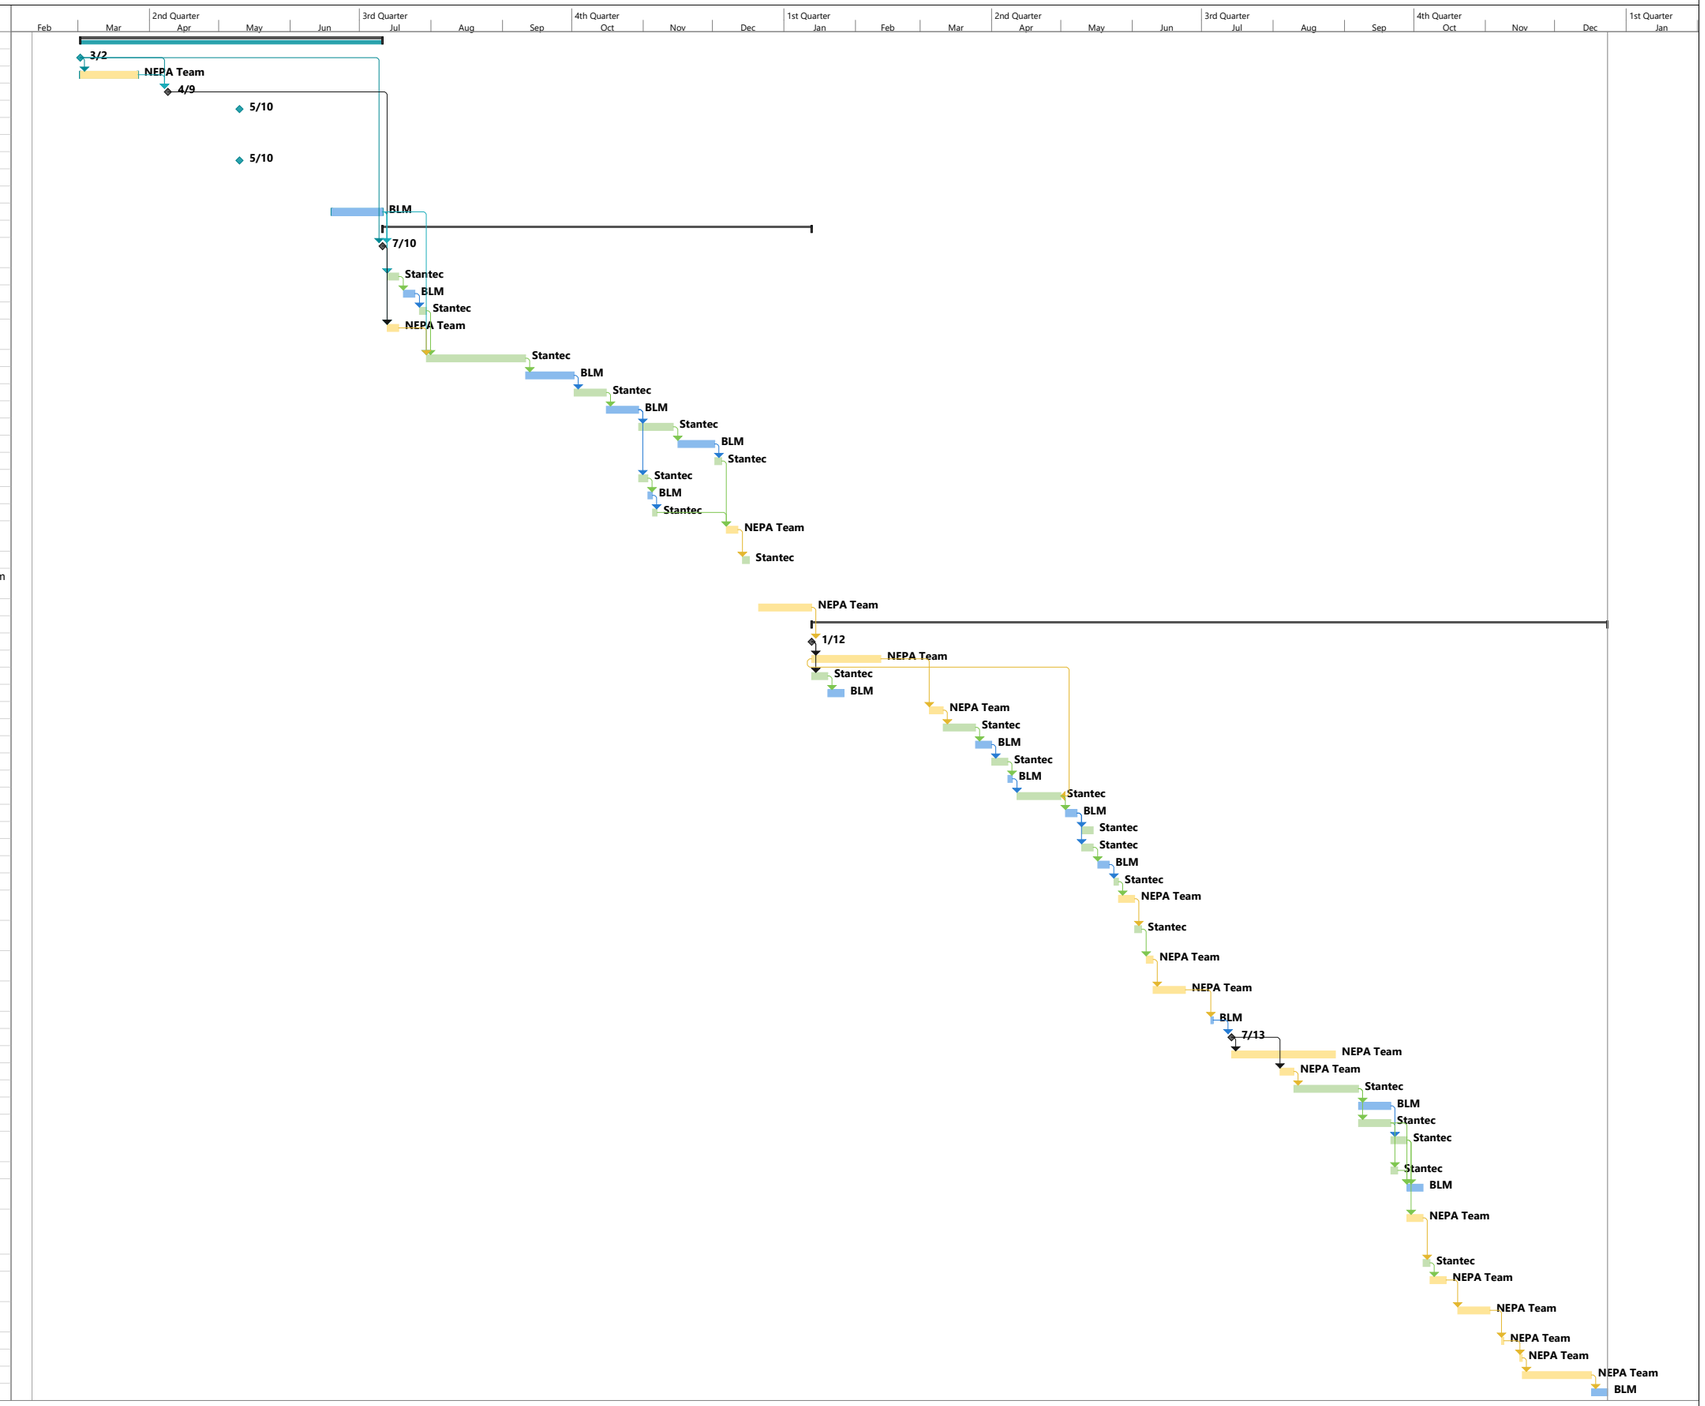

Project: Rhyolite Ridge EIS
Date: Wed 5/27/20

BLM Stantec NEPA Team
